


# High Level Banner 9 (XE) Timeline

A-State

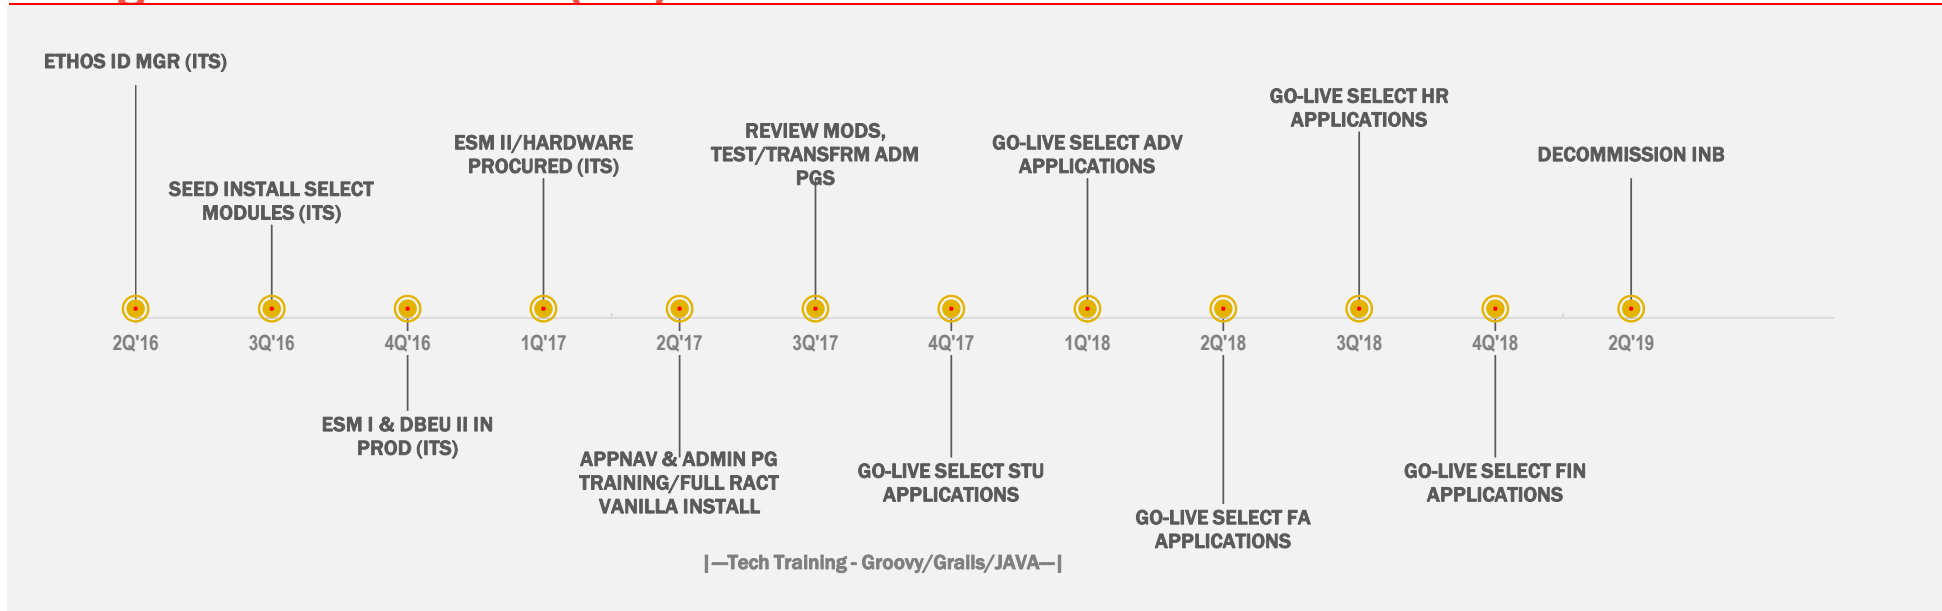

## PROJECT DETAILS

DATE	MILESTONE
2Q'16	Ethos ID Mgr (ITS)
3Q'16	Seed install select modules (ITS)
4Q'16	ESM I & DBEU II in PROD (ITS)
1Q'17	ESM II/Hardware procured (ITS)
2Q'17	AppNav & Admin Pg Training/full RA
3Q'17	Review Mods, test/transfrm Adm Pgs
4Q'17	Go-live select STU applications
1Q'18	Go-live select ADV applications
2Q'18	Go-live select FA applications
3Q'18	Go-live select HR applications
4Q'18	Go-live select FIN applications
2Q'19	Decommission INB

\* INB is now called Admin Pages

\* Sequencing of go-live modules subject to change

## FUNCTIONAL DEPARTMENTS DETAIL

DATE	MILESTONE
2Q'16	
3Q'16	
4Q'16	
1Q'17	Various campus users attend the Ellucian Live Conference
2Q'17	Depts review XE documentation, est Lead & training plan
3Q'17	Depts begin to review, test transformed Admin Pgs, train
4Q'17	STU - go live monitor, review, lessons learned.
1Q'18	ADV - meet with STU review lessons learned, go live.
2Q'18	FA - meet with STU & ADV review lessons learned, go live.
3Q'18	HR-meet with STU, ADV, FA review lessons learned, go live.
4Q'18	FIN-meet STU, ADV, FA, HR review lessons learned, go live.
2Q'19	Decommission INB

\* 2Q'17 - ITS will begin bi-weekly meetings with Dept Leads to provide training docs, videos, on-going support, and to plan.
